

## Katherine Warrington School

Welcome to the fourth communications update from Kier. These regular publications will keep you updated with progress on site and what to expect in the months ahead. We will highlight recent construction works, as well as what to expect in the upcoming months.

### About the project

Kier has been appointed by the Department for Education to construct a two-storey sports hall and a two-storey secondary school. Externally, the project also includes a number of soft sports playing areas, a Multi-Use Games Area (MUGA) and hard landscaped areas to form car parking and footpaths. The project is split into three phases with phase one being completion of the temporary school within the sports hall, phase two being completion of the main school and phase three being converting the temporary school back into a sports hall.

### Progress update

Once again, the fine spring weather has been on our side and we are still on target to meet the agreed contractual completion date for Phase 1 (the temporary school) for handover during September 2019. Structural toppings have now been installed onto the concrete plank floors on the sports hall and works can now commence on installing the facade. In tandem with this, internal works will commence once the roof has been completed and the building is watertight. Elsewhere on the site the main school steel frame is rapidly being constructed. with concrete plank floors booked for an early June installation.

Over the coming weeks works to the sports hall will continue to concentrate on the façade and roof, with the main school receiving its concrete plank floors and roof slab, both of which are booked for an early June installation.



### Contact us

We look forward to being your neighbours and welcome your feedback or questions. Our nominated site contact is Senior Site Manager, Andy Gruncell.

e: [KCE.Harpendencommunity@kier.co.uk](mailto:KCE.Harpendencommunity@kier.co.uk)

t: 07583 105704

Andy can be contacted during normal working hours.

### Write to us

Alternatively, you can write to us at our main office:

Kier Construction  
Cambridge Research Park  
Waterbeach  
Cambridgeshire  
CB25 9PD

t: 01223 205 900

### Programme of works

June:  
Main School  
Concrete Floors

July:  
Internals to  
Sports Hall

Aug:  
Sports Hall  
Internal &  
External Works

Sept:  
SFS and  
Windows to Main  
School

## Our Project Team



**Contracts Manager**  
Allan Craig



**Senior Project Manager**  
David Tomlin



**Senior Site Manager**  
Andrew Gruncell



**Site Manager**  
Liam Tracy



**Engineer**  
Asish Chauhan



**Senior Quantity Surveyor**  
Steven Sylvester

## Considerate Constructors

The site is registered with the Considerate Constructors Scheme, which is an independently audited assessment of a project's consideration for the local community, its operatives and the environment.

As part of our commitment, we do what we can to minimise disruption from the project. If you have any concerns, please do not hesitate to contact us.




## Message from the Project Manager

Our community webpage has proved positive to date and during next month one of the local students by request, will be joining us on site for work experience which is excellent news for the project team. As always you can email the project team direct at [KCE.Harpdencommunity@kier.co.uk](mailto:KCE.Harpdencommunity@kier.co.uk) or use the contact link on our project webpage. The webpage address is:

<http://www.kier-constructioneastern.co.uk/home/katherine-warington/>

As always, I would ask that children are reminded that construction sites can be dangerous and that they are discouraged from entering the site.

**Coming soon: updates relating to the upcoming S278 works which includes some major highways improvements in the vicinity of the new school.**

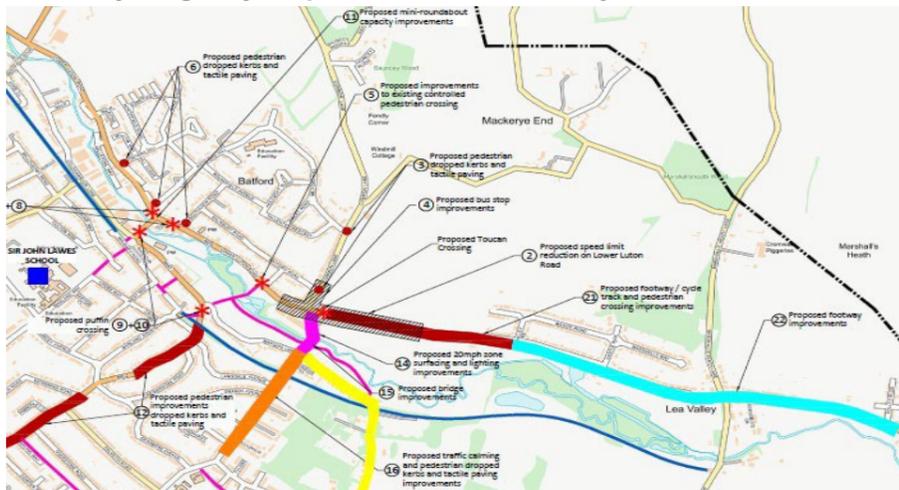

## Working hours:

Our general working hours are 07:30 - 18:00 Monday to Friday. Occasionally, we may work on Saturday mornings from 08:00 - 13:00.

## Car Parking:

The Kier site team and contractors will park in the dedicated contractors parking facilities located within the site compound.

## Deliveries and site traffic:

All deliveries are pre-booked and within site working hours and wherever possible are planned to avoid highly congested periods.

We will have a full time Gateman at the site entrance to control and direct deliveries. All deliveries are directed straight into site to avoid disturbance and traffic congestion.

**To date 98% of waste generated on this project has been diverted from landfill.**

**Thank you for taking the time to read this newsletter.**



Kierconstruct
